


ID		EDT	Task Name	Duration	Work	Cost	Start	Finish	Predeces	Resource Names
1			Proyecto	59 days	372 hrs	13.915,40 €	Mon 29/09/25	Fri 05/12/25		Reserva de contingencia[1]
2	✓	1	Inicio	6 days	36 hrs	1.357,92 €	Mon 29/09/25	Sat 04/10/25		
3	✓	1.1	Conocimientos previos	6 days	36 hrs	1.357,92 €	Mon 29/09/25	Sat 04/10/25		Gestor de documentación/Analista
4	✓	2	Planificación	23 days	138 hrs	5.205,36 €	Mon 06/10/25	Fri 31/10/25		
5	✓	2.1	Documentos de gestión	11 days	66 hrs	2.489,52 €	Mon 06/10/25	Fri 17/10/25		Gestor de documentación/Analista
6	✓	2.2	Documentos de ejecución	12 days	72 hrs	2.715,84 €	Sat 18/10/25	Fri 31/10/25	5	Gestor de documentación/Analista
7		3	Desarrollo	18 days	150 hrs	4.541,56 €	Mon 03/11/25	Sat 22/11/25		Servidor PaaS[1];Software de de
8	✓	3.1	Iteración 1	6 days	48 hrs	1.403,40 €	Mon 03/11/25	Sat 08/11/25		
9	✓	3.1.1	Mockups	1 day	6 hrs	186,36 €	Mon 03/11/25	Mon 03/11/25		Desarrollador Full-Stack
10	✓	3.1.2	Creación Base de	2 days	12 hrs	372,72 €	Mon 03/11/25	Tue 04/11/25		Desarrollador Full-Stack
11	✓	3.1.3	Información corporativa y legales de Essenza	1 day	6 hrs	186,36 €	Tue 04/11/25	Tue 04/11/25	9	Desarrollador Full-Stack
12	✓	3.1.4	Gestión del usuario	2 days	12 hrs	372,72 €	Wed 05/11/25	Thu 06/11/25	10	Desarrollador Full-Stack
13	✓	3.1.5	Ejecución pruebas 1	2 days	12 hrs	285,24 €	Fri 07/11/25	Sat 08/11/25	12	Tester de calidad
14	✓	3.2	Iteración 2	6 days	54 hrs	1.589,76 €	Mon 10/11/25	Sat 15/11/25	8	
15	✓	3.2.1	Cliente	3 days	18 hrs	559,08 €	Mon 10/11/25	Wed 12/11/25		

Project: Project1
Date: Thu 20/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	


ID		EDT	Task Name	Duration	Work	Cost	Start	Finish	Predecessors	Resource Names
16	✓	3.2.1.1	Catálogo de	1 day	6 hrs	186,36 €	Mon 10/11/25	Mon 10/11/25		Desarrollador Full-Stack
17	✓	3.2.1.2	Escaparate y	2 days	12 hrs	372,72 €	Tue 11/11/25	Wed 12/11/25	16	Desarrollador Full-Stack
18	✓	3.2.2	Administración	2 days	24 hrs	745,44 €	Mon 10/11/25	Tue 11/11/25		
19	✓	3.2.2.1	CRUD productos	2 days	12 hrs	372,72 €	Mon 10/11/25	Tue 11/11/25		Desarrollador Full-Stack
20	✓	3.2.2.2	Stock de productos	2 days	12 hrs	372,72 €	Mon 10/11/25	Tue 11/11/25		Desarrollador Full-Stack
21	✓	3.2.3	Ejecutar pruebas 2	2 days	12 hrs	285,24 €	Thu 13/11/25	Fri 14/11/25	15;18	Tester de calidad
22		3.3	Iteración 3	6 days	48 hrs	1.403,40 €	Mon 17/11/25	Sat 22/11/25	14	
23		3.3.1	Cliente	4 days	30 hrs	931,80 €	Mon 17/11/25	Thu 20/11/25		
24		3.3.1.1	CRUD carrito	2 days	12 hrs	372,72 €	Mon 17/11/25	Tue 18/11/25		Desarrollador Full-Stack
25		3.3.1.2	Información del	1 day	6 hrs	186,36 €	Mon 17/11/25	Mon 17/11/25		Desarrollador Full-Stack
26		3.3.1.3	Checkout	2 days	12 hrs	372,72 €	Wed 19/11/25	Thu 20/11/25	24	Desarrollador Full-Stack
27		3.3.2	Administración	1 day	6 hrs	186,36 €	Mon 17/11/25	Mon 17/11/25		
28		3.3.2.1	Listado de todos	1 day	6 hrs	186,36 €	Mon 17/11/25	Mon 17/11/25		Desarrollador Full-Stack
29		3.3.3	Ejecutar pruebas 3	2 days	12 hrs	285,24 €	Fri 21/11/25	Sat 22/11/25	23;27	Tester de calidad
30		4	Seguimiento y Control	5,5 days	24 hrs	905,28 €	Mon 24/11/25	Fri 28/11/25	7	


Project: Project1
Date: Thu 20/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

ID		EDT	Task Name	Duration	Work	Cost	Start	Finish	Precedes	Resource Names
31		4.1	Informes de seguimiento	4 days	24 hrs	905,28 €	Mon 24/11/25	Thu 27/11/25		Gestor de documentación/Analista
32		5	Cierre	4 days	24 hrs	905,28 €	Mon 01/12/25	Thu 04/12/25	30	
33		5.1	Informes y lecciones aprendidas	4 days	24 hrs	905,28 €	Sat 29/11/25	Wed 03/12/25		Gestor de documentación/Analista

Project: Project1 Date: Thu 20/11/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

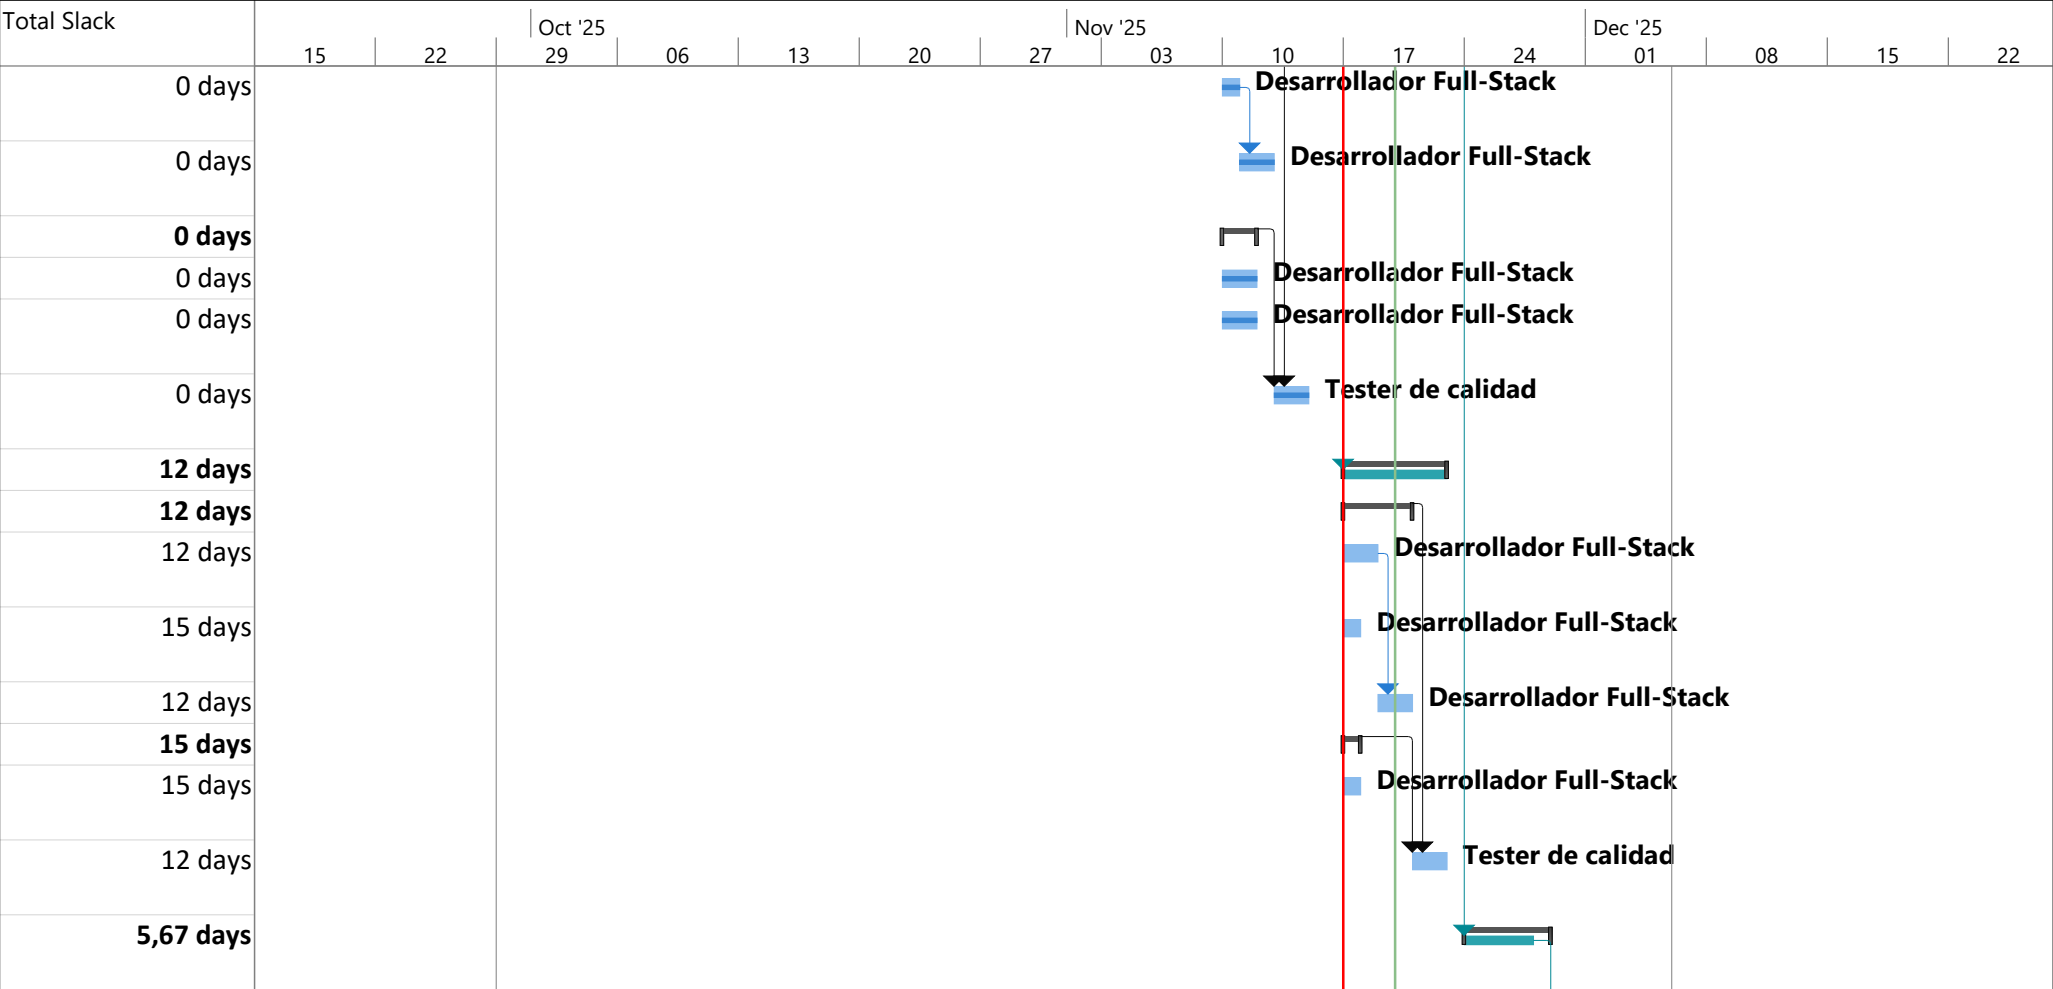

Project: Project1 Date: Thu 20/11/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	



Project: Project1 Date: Thu 20/11/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

