

ID	Name	Duración	Holgura	BAC	% Complete	PV	EV	AC	CV	15	22	Oct '2
1	Proyecto	15,23 d...	0 days	0,00 €	74%	0,00 €	0,00 €	9.556,44 €	-9.556,4...			
2	Inicio	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	1.357,92 €	-1.357,9...			
3	Conocimientos previos	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	1.357,92 €	-1.357,92 €			
4	Planificación	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	5.205,36 €	-5.205,3...			
5	Documentos de gestión	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	2.489,52 €	-2.489,52 €			
6	Documentos de ejecución	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	2.715,84 €	-2.715,84 €			
7	Desarrollo	5,76 days	12 days	0,00 €	68%	0,00 €	0,00 €	2.993,16 €	-2.993,1...			
8	Iteración 1	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	1.403,40 €	-1.403,4...			
9	Mockups	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	186,36 €	-186,36 €			
10	Creación Base de Datos	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	372,72 €	-372,72 €			
11	Información corporativa y legales de Essenza	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	186,36 €	-186,36 €			
12	Gestión del usuario	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	372,72 €	-372,72 €			
13	Ejecución pruebas 1	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	285,24 €	-285,24 €			
14	Iteración 2	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	1.589,76 €	-1.589,7...			
15	Cliente	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	559,08 €	-559,08 €			

Project: Project1
Date: Thu 20/11/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split


Progress

Manual Progress



Page 1

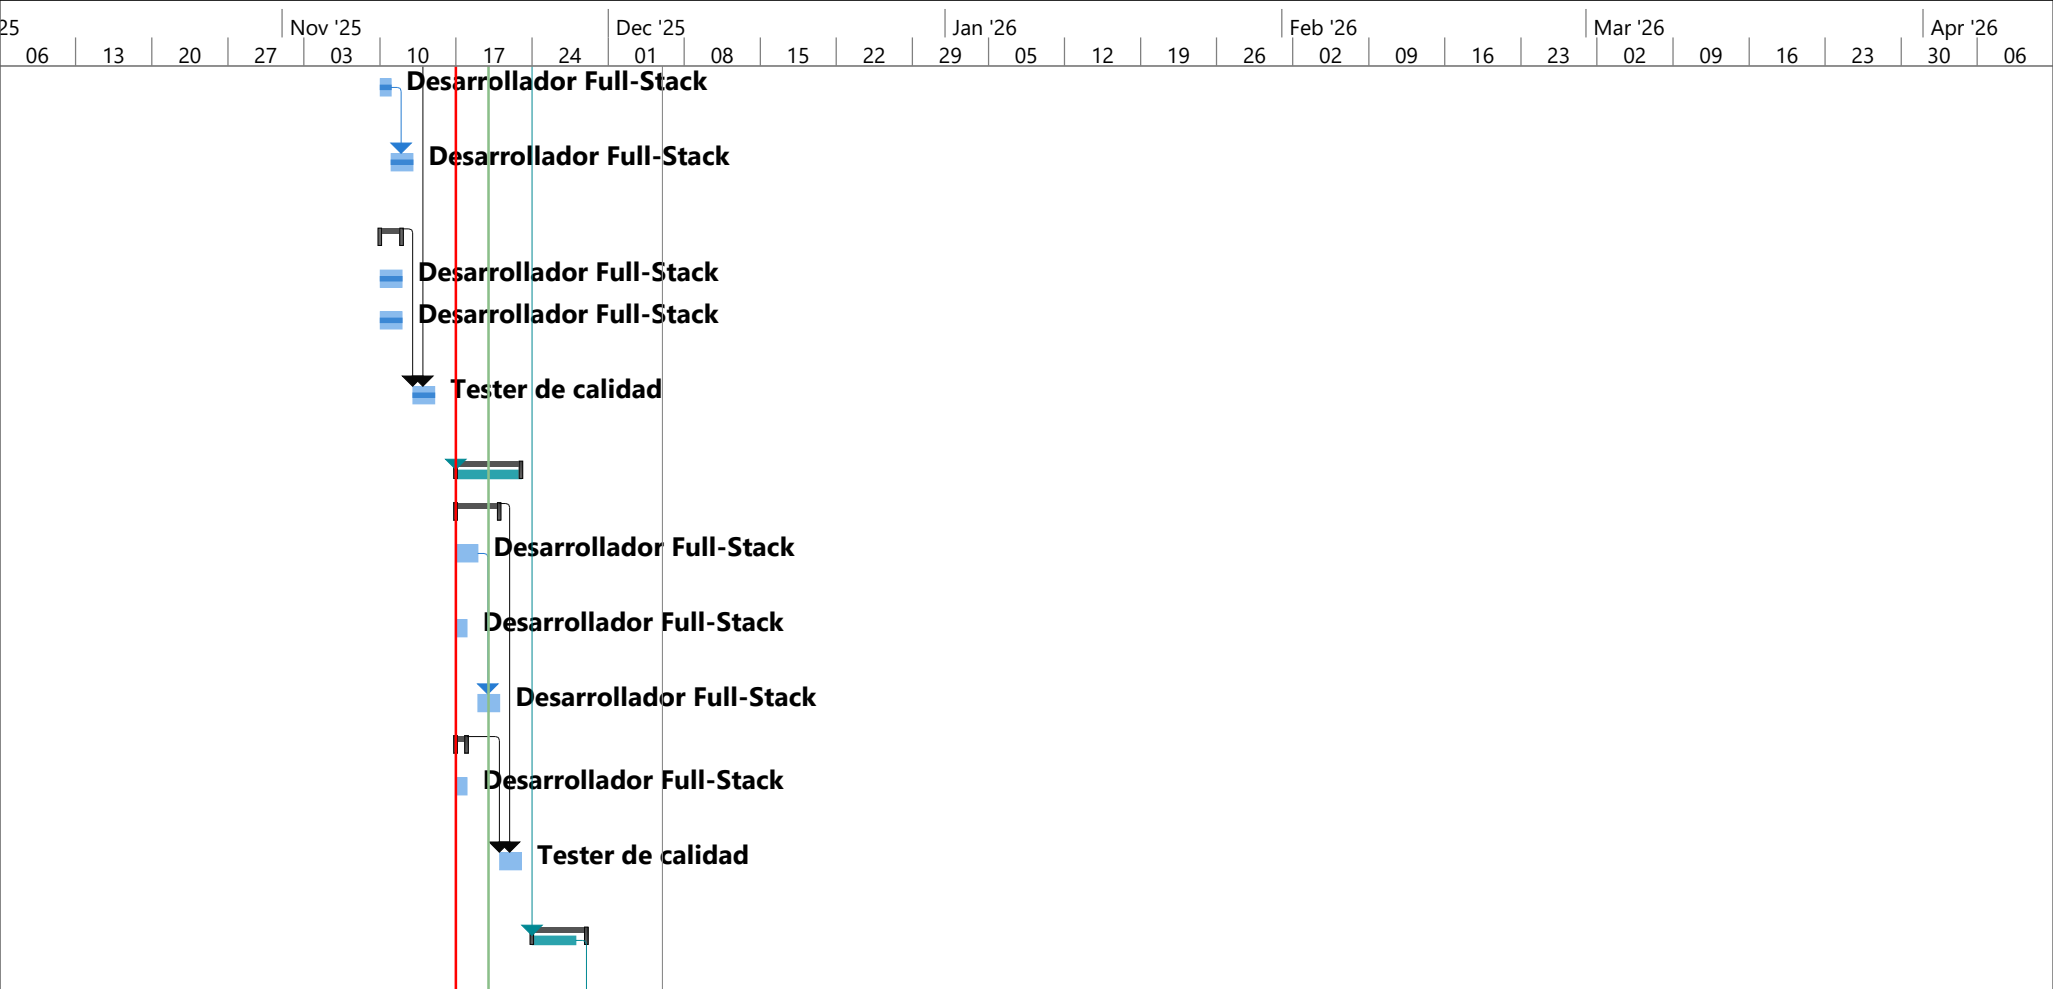
ID	Name	Duración	Holgura	BAC	% Complete	PV	EV	AC	CV	15	22	Oct '2
16	Catálogo de productos	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	186,36 €	-186,36 €			
17	Escaparate y navegación	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	372,72 €	-372,72 €			
18	Administrador	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	745,44 €	-745,44 €			
19	CRUD producto	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	372,72 €	-372,72 €			
20	Stock de productos	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	372,72 €	-372,72 €			
21	Ejecutar pruebas 2	0 days	0 days	0,00 €	100%	0,00 €	0,00 €	285,24 €	-285,24 €			
22	Iteración 3	6 days	12 days	0,00 €	0%	0,00 €	0,00 €	0,00 €	0,00 €			
23	Cliente	4 days	12 days	0,00 €	0%	0,00 €	0,00 €	0,00 €	0,00 €			
24	CRUD carrito compra	2 days	12 days	0,00 €	0%	0,00 €	0,00 €	0,00 €	0,00 €			
25	Información del pedido	1 day	15 days	0,00 €	0%	0,00 €	0,00 €	0,00 €	0,00 €			
26	Checkout	2 days	12 days	0,00 €	0%	0,00 €	0,00 €	0,00 €	0,00 €			
27	Administrador	1 day	15 days	0,00 €	0%	0,00 €	0,00 €	0,00 €	0,00 €			
28	Listado de todos los	1 day	15 days	0,00 €	0%	0,00 €	0,00 €	0,00 €	0,00 €			
29	Ejecutar pruebas 3	2 days	12 days	0,00 €	0%	0,00 €	0,00 €	0,00 €	0,00 €			
30	Seguimiento y Control	5,5 days	5,67 days	1.802,40 €	0%	1.802,40 €	0,00 €	0,00 €	0,00 €			

Project: Project1
Date: Thu 20/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	


ID	Name	Duración	Holgura	BAC	% Complete	PV	EV	AC	CV	15	22	Oct '2
31	Informes de seguimiento	4 days	6,67 days	0,00 €	0%	0,00 €	0,00 €	0,00 €	0,00 €			
32	Cierre	4 days	0,67 days	4.904,00 €	0%	4.904,00 €	0,00 €	0,00 €	0,00 €			
33	Informes y lecciones aprendidas	4 days	1,67 days	3.136,00 €	0%	3.136,00 €	0,00 €	0,00 €	0,00 €			

Project: Project1 Date: Thu 20/11/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	



Project: Project1 Date: Thu 20/11/25	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	


Project: Project1
Date: Thu 20/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

Project: Project1
Date: Thu 20/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

Project: Project1
Date: Thu 20/11/25

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	
